M- 12/27-14

3人.

3 9349 00392 1273

USAF PLAN OF ACTION FOR THE

PHASE-OUT AND DISPOSITION OF

THE ATLAS E, ATLAS F, AND TITAN I

(20 JANUARY 1965)

COORDINATION SHEET

USAF PLAN OF ACTION FOR THE PHASE-OUT AND DISPOSITION OF THE ATLAS E, ATLAS F, AND TITAN I

AFLC COORDINATION

H. C. Porter
Major General, USAF
Chief of Staff

ATC COORDINATION

W. W. Momyer Lt General, USAF

ATCCR 00009 Message, dated 6 January 1965. Concur with proposed USAF Plan of Action for Missile Phase Out as finalized at your Headquarters on 30 Dec 64.

ATXPP-G 69032 Message, dated 18 January 1965, indicates concurrence in below referenced message MCGM 5007; also additional changes proposed by ATC have been incorporated in this plan.

SAC COORDINATION

DPL 03314 Message, dated 13 January 1965. The USAF Plan of Action for the Phase-Out and Disposition of the Atlas E, F and Titan I, which was finalized by AFLC/SAC/ATC representatives at Hq AFLC on 30 Dec 64, has been reviewed by this Hq and is concurred in provided the following changes/additions are made.

MCGM 5007 Message, dated 15 January 1965 indicates SAC concurrence with revisions to the changes.

Recommended changes have been incorporated in the body of the plan.

FOREWORD

The attached phase-out plan has been prepared in accordance with AFLC message MCOOS 1980, dated 24 July 1964, and AFCVC message 96605, dated 8 December 1964.

PLAN OF ACTION

USAF Plan for Phase-Out and Disposition of the ATLAS E, F and Titan I Operational Systems.

TABLE OF CONTENTS

Paragraph	Title	Page	Nr.
1.	Directive and Guidance	- 1	
2.	Objectives	1	
3.	Factual Data	2	
L.	Assumptions	4	
5.	Ground Rules	6	
6.	Assignment of Tasks	8	
7.	Effective Date of Plan	12	
TAB A	Reference Messages	13	
TAB B	Atlas E Data	15	
TAB C	Atlas F Data	21	
TAB D	Titan I Data	28	

1. DIRECTION AND GUIDANCE:

The direction and guidance for this plan is contained in PCP 64-60, 64-61 and other Directives/messages contained in Tab A. It is anticipated that additional implementing direction will be in the form of Operations Plans, Base Support Agreements, Local Operation Procedures, etc.

2. OBJECTIVES:

To insure an effective, orderly phase-out, attrition/utilization and disposition of the ATLAS E, F and TITAN I operational system assets realizing a maximum dollar return to the Air Force/DOD.

3. FACTUAL DATA:

- a. System Documentation is contained in:
- (1) Atlas System Package Program, 10 Dec 62, as revised; SPD 107A-65-1, 20 Nov 64.
- (2) Titan I: System Package Program, 10 Dec 62, as revised; SPD 107B/C-65-2, 23 Dec 64.

b. This plan applies to the Atlas E, F and Titan I operational systems with the exception of Vandenberg Air Force Base and Sheppard Air Force Base Missile Training facilities.

(1) ATLAS E Operational System:

567th SMS Fairchild AFB

548th SMS Forbes AFB

566th SMS Warren AFB

(2) ATLAS F Operational System:

550th SMS Schilling AFB

551st SMS Lincoln AFB

577th SMS Altus AFB

578th SMS Dyess AFB

579th SMS Walker AFB

556th SMS Plattsburgh AFB

(3) TITAN I Operational System:

724th SMS Lowry AFB

725th SMS Lowry AFB

569th SMS Mt. Home AFB

850th SMS Ellsworth AFB

568th SMS Larson AFB

851st SMS Beale AFB

- (4) In the event certain Vandenberg/ATC facilities are declared excess to USAF requirement, disposition actions will generally be as outlined herein.
- c. The Airborne Vehicle contains an airframe with propulsion system, guidance system, re-entry vehicle and flight control system.
- d. The AGE primarily consists of Missile Launcher, Launch Control Equipment,
 Checkout Equipment, Guidance Equipment, Power and Maintenance Equipment,
 Communication, Propellant Loading.
- e. Receiving facilities are contained in the missile assembly and maintenance shop (MAMS).
- f. The RPIE sub-systems are identified as Air Conditioning, Power

 Generation and Distribution, Water Pumping and Distribution, Utility Air System,

 LOX/RP-1 and Diesel Vapor Detection System, Blast Detection, Flame Tunnel,

 Overhead Handling System, Waste Disposal System, Security System, LCC Silo

 Suspension System, and Personnel Elevator.
 - g. Communication System, i.e., HG/UHG, SSB, Radios, TV system.
- h. The Atlas E, F and Titan I Systems have completed the operational phase. These systems will no longer be required for combat operation.

4. ASSUMPTIONS:

- a. SAC will develop and USAF will approve the ATLAS and TITAN I complex alert removal schedules.
- b. AFSC and other Air Force activities will utilize the Airborne Booster, selected AGE and supporting range of Spare Parts (Airborne, RPIE and AGE) for future programs, e.g., (ABRES/NIKE etc.) where possible.
- c. System Peculiar End Items, Spares and operational residue will be disposed of as prescribed in para 6 of this plan. Common End Items and Spares will be retained where required to support continuing operational programs.
- d. There will be Airborne and Installed AGE items for which there is no continuing requirement, which, because of security or proprietary implications must be demilitarized or destroyed under Air Force supervision. Reference AFM 67-1, Vol VI, Chapter 10.
- e. AGE, RPIE, Airborne Items, C-E-M Items and associated spares will be disposed of through proper channels: IM, DSA, Base R&M, etc., in accordance with this plan and existing directives to insure maximum use or dollar return to the Air Force.
- f. Existing SAC personnel and equipment will be used to remove and ship missiles and classified items, RV, Cryogenics/gases as required, mobile AGE and USAF Save List Items (identified by

AFLC). SAC may require AFLC Maintenance/Engineering assistance (T.O. 00-25-107), specialized engineering and/or planning assistance during dismantling, removal and packaging of such items.

AFLC). SAC may require AFLC Maintenance/Engineering assistance (T.O. 00-25-107), specialized engineering and/or planning assistance during dismantling, removal and packaging of such items.

- g. SAC assigned personnel will remain as SAC resources and be reassigned in accordance with AFM 35-11 and 39-11. AFLC will provide SAC with mutually developed minimum standards for preservation of facilities after completion of SAC actions stated in paragraph 4f. SAC will retain at each base sufficient personnel to accomplish missile site preservation. Transfer of some SAC personnel to other Commands will be required to accomplish this function.
- h. The existing DOD/USAF/AFLC/SAC organizations established for reclamation and disposal of Air Force property will be used to accomplish this task.
- i. No further Air Force utilization is currently programmed for facility or real estate at the operational site.
- j. A minimum expenditure of Air Force funds will be made to restore to safe condition and dispose of the operational facilities and real estate.
- k. The System Support Manager (SSM) will be relieved of Operational Support responsibility upon removal of the weapon systems from Alert Status.
- 1. The Host Base will retain Real Property title and provide necessary government equipment preservation/environmental control pending receipt of disposal and/or transfer instructions for the ICBM off-base installations. Appropriate SAC/ATC personnel will be retained to insure compliance with USAF approved care and custody standards.

5. GROUND RULES:

- a. AFSC with assistance from AFLC and SAC will develop plans for future utilization of Atlas E, F and Titan I resources which become excess to operational requirements.
- b. Assets will be screened and redistributed in the following order of precedence:
 - (1) USAF Operational force requirements.
- (2) Excess to USAF operational requirements, but required by other Air Force agencies.
- (3) Excess to AF requirements, but required by other DOD agencies.
- (4) Excess to AF and DOD requirements, but required by other government agencies.
 - (5) Other (Schools, cities, R&M, etc.)
- c. Existing regulations as modified and amplified by USAF message, AFCVC 96605, dated 8 Dec 64, and this plan will apply.
- d. Schedules will be compressed where possible to provide for concurrent screening by Air Force, DOD and other government agencies.
- e. Available USAF "Blue Suit" personnel will be utilized where possible to reduce costs.
- f. Materiel which is excess to the missile programs will be used in other programs to preclude new buys.
- g. Site security will be reduced to "Surveillance Only" after classified removal and commensurate with accountability requirement.

- h. AFLC will assume executive management responsibility for the disposition of system assets, including RPIE, but excluding other real property which will be disposed of in accordance with existing instructions.
- i. AFLC will establish a Deactivation Task Force to monitor and control the disposition processes to include DOD and other governmental agency screening of excess assets, scheduling for removal of items, provision of engineering support and necessary GEEIA support.
- j. AFLC will establish at each base a military representative as the Executive Manager to assume operational control of the personnel to be provided by SAC/ATC. Operational control for the purpose of this plan is defined as that technical guidance and direction necessary to assure the preservation, dismantling, and orderly economic disposition of weapon system assets. He will assume the above responsibilities at such time as mutually agreed upon by SAC/ATC/AFLC.
- k. SAC will provide personnel support to the AFLC Deactivation Task Force Commander, both at AFLC and at each base (150-200 personnel at each base).
- 1. MAC Host Bases will retain responsibility and accountability for equipment and facilities pending appropriate disposition.
- m. Host Base support agreements will be prepared in accordance with AFR 11-4.

- n. SAC Units will utilize locally developed inactivation operations plans as necessary to augment this plan.
- o. Hq USAF will provide funding beyond Major Air Command capabilities.

ASSIGNMENT OF TASKS: To accomplish the objectives of this plan within the parameters established in USAF, AFCVC 96605, dated 9 December 64, the following tasks are assigned:

following tasks	are assigned:	
TARGET DATE	ACTIVITY	ASSIGNED TASKS
TARGET DATE	AFLC	Establish a Headquarters Deactivation Task
	11 10	Force to monitor and control the disposition
		processes to include DOD and other govern-
		mental agency screening of excess assets,
		scheduling for removal of items and provision
		for engineering support.
	AFLC	Assume management responsibility for the
		disposition of Systems Assets.
	AFLC/SAC/AFSC	Establish focal points at each Headquarters
	ATC	for inputs to this plan and for controlling
	*	and accomplishing actions as detailed herein.
	AFLC/SAC/AFSC	Prepare implementing plans to support this
	ATC	plan as required.
	SAC	Establish and secure USAF approval of a
		phase-out schedule by complex.
	AFLC	Establish at each base an AFLC military rep-
		resentative of appropriate rank responsive
		only to the Hq, AFLC Task Force Commander.
		This representative will assume operational
		control of a local task force to be provided
		by SAC/ATC to be utilized in the care/custody/
		disposal of materiel. The AFLC local task
8		force commander will assume the responsibility

SAC/ATC

AFLC/MAC

AFLC/SAC/

SAC/ATC/AFLC

(SBAMA)

ATC

ASSIGNED TASKS

for control of all disposal processes relating to organizational materiel and equipment, including RPIE, in accordance with approved policies and procedures. Additionally, he will be responsible to assure the provision of adequate environmental control and such care as may be required until the sites have been reported to GSA for disposition.

USAF Approve phase-out schedule and reallocate boosters.

Prepare Brochure material for submission

to DSA.

DLSC Publish and distribute brochure for DOD and other government agency screening.

SAC Redistribute excesses within MAC in accordance with AFM 67-1.

Establish critical Item Requirements (AGE, RPIE, C-E-M) to take action to schedule removal and redistribution as applicable.

Provide transportation coordination for timely missile movement.

	*				
ACTIVITY	ASSIGNED TASKS				
AFLC	Provide adequate storage facilities				
	for phase-down missiles.				
AFLC	Establish materiel requirements to				
24	support future booster utilization.				
	Transportation funding for surface				
	and air movement of missiles from				
	missile sites/host bases is an AFLC				
	responsibility.				
SAC	Remove missiles, RV, cryogenics/gasses,				
	classified materiel, and Save List				
	items.				
SAC/AFLC	Detailed preservation tasks will be				
(SBAMA)	developed jointly by SAC and AFLC.				
AFLC	Provide surveillance and direction				
	for the disposition of AGE Save List				
	requirements.				
SAC/AFLC/ DSA	Provide redistribution of remaining				
DSA	asset requirements in accordance with				
	established priorities. Non-mobile				
	AGE, C-E-M and RPIE normally will be				
	left in-place while being circularized				
	for other than Host Base requirements.				
	Funding for the dismantling, removing,				

TARGET DATE

ASSIGNED TASKS

and packing of equipment excess to

USAF IM programmed operational

requirements is the responsibility of
the gaining agency. Transportation

costs for movement of this equipment
to another Air Force agency will be
borne by the shipping activity.

Transportation costs for movement to
other than AF agencies will be borne
by the gaining agency.

AFLC

Provide transportation management services for airlift and commercial over-the-road movement of missiles from missile sites/host bases.

Insure the availability of missile trailers to meet AFLC/SAC shipment schedules.

ACTIVITY	ASSIGNED TASKS
MAC/Host Base	Provide for disposal of residue materiel/
	facilities/real estate in accordance with
	existing directives (AFR 87-4) or by other
	USAF direction.
SAC	Deactivate ICBM squadrons in accordance
	with USAF program.
AFLC/SAC	Develop appropriate plans and procedures to
	determine the exact systems, subsystems and
	components that must remain operational in
	order to preserve life expectancy of the
	government equipment at the site after EWO
	status and forward same to Hq USAF for
	approval.
Host Base	Will provide administrative support to the
	local task force commander as is required.
Host Base	Provide site security as determined to be
	necessary by Base Commander, through the
	phase-out and as required in support of GSA.
Host Base	Provide utility services as necessary.
Host Base	Retain accountability of all property
	until transfer to the receiving organization.
SAC/MAC	Redesignate as RPIE for disposal purposes only,

residual non-mobile AGE and C-E-M equipment

TARGET DATE

left in-place during excess screening process and for which no requirement was identified. BEMO/COMM/Civil Engineer records will be adjusted accordingly.

SAC/AFLC/ATC

Determine funds requirements and provide

appropriate justification.

USAF

Provide funding beyond Major Air Command

7. Effective Date of Plan:

This plan is effective for planning upon receipt and for implementation upon USAF approval. All Commands will coordinate with other participating Commands on implementation and completion of assigned tasks.

capabilities.

Reference Documents and Messages

- 1. USAF PG 66-3 June 1964 (S)

 Reflects ATLAS "E" and TITAN I phase out dates in accordance with PCP 64-60 and PCP 64-61.
- 2. Hq USAF PA 66-3

 Reflects ATLAS "E" and TITAN I phase out dates in accordance with PCP 64-60 and PCP 64-61.
- 3. CSAF (AFOAPB) 83491 2 June 1964 (S)
 Establishes program life for life-of-type computation for ATLAS "F"
 inertial guidance system.
- 4. AF SSSCB/AFSPDB 83926 3 June 1964 (S)

 Directs, no further spares procurement be made for ATLAS "D", "E" and TITAN I except for NORS.
- 5. AFLC (MCG) 1538 9 June 1964 (S)

 Reflects proposed ATLAS "E" and TITAN I phase out dates and directs
 a review of contracts preparatory to decommitment action.
- 6. PCP 64-60 9 July 1964 (S)

 Provides proposed phase out dates for ATLAS "E" and "F" weapon systems.
- 7. PCP 64-61 9 July 1964 (S)

 Provides proposed phase out dates for TITAN I weapon system.
- 8. AFLC (MCOOS) 1980 24 July 1964 (S)

 Directs SBAMA in conjunction with SAC and BSD to develop ATLAS "E" and TITAN I phase out plans.

- 9. CSAF (AFSPDB) 92162 21 November 1964 (U)

 Furnishes SPD WS 107A-65-1 (ATLAS) which directs program changes

 for the phase out of ATLAS "E" and "F" forces during the last half


 of FY-65.
- 10. SPD WS 107B/C-65-2

 22 December 1964 (S)

 This SPD directs the program changes for the phase out of the TITAN I force during the last half of FY-65.
- 11. USAF (AFCVC) 96605 8 December 1964 (U)

 Furnishes the policies and assigned the Command responsibilities for
 the disposal of missile complexes and material and additionally directs
 that detailed phase out plans be submitted to USAF for approval.

IX9 CONFIGURATION, INERTIAL GUIDANCE (TYPICAL) 567, 1 548, 1 8 566 1 STRATEGIC MISSILE SQUADRONS

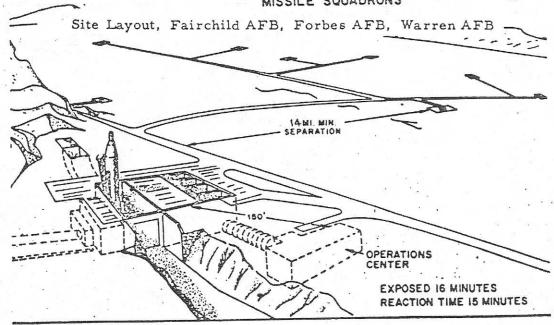

ATLAS "E" LOCATIONS

	566 SMS F. E. WARREN		548 SMS FORBES		567 SMS FAIRCHILD	
	60-5518	(60E)	60-5512	(54E)	58-7131	(15E)
	60-5516	(58E)	60-5521	(63E)	60-5500	(42E)
305	60-5511	(53E)	60-5517	(59E)	60-5489	(31E)
	60-5510	(52E)	60-5508	(50E)	60-7130	(14E)
	60-5509	(51E)	60-5507	(49E)	60-5499	(41E)
	60-5513	(55E)	60-5503	(45E)	58-7135	(19E)
	60-5492	(34E)	60-5496	(38E)	60-5497	(39E)
	62-12124	(73E)	60-5491	(33E)	60-5495	(37E)
	61-2522	(68E)	62-12436	(75E)	60-5487	(29E)
	60-5501	-(43E)	58-7139	(23E)	62-12437	(76E)
	SBAMA S	TORAGE	GD/A ST	ORAGE	ATC	
	60-5504	46E	62-12435	74E	58-7126	10E
	58-7123	7E	62-12438	77E		
	58-7127	11E	62-12439	78E		
	60-5486	28E				
	60-5502 44E				VANDENI	
	60-5519	61E			58-7136	(20E)
	60-5414	56E				
	58-7136	20€				

1. Operational Missile Area Sub-System (Ground)

Included in this broad category are two basic subdivisions: The operational Ground Equipment which must operate successfully with the missile during readiness, count down and launch, and the Maintenance Ground Equipment which is required to receive, service, maintain and verify the missiles and related equipment.

(1) For series E, the following major elements comprise the OGE:

a. Operational Ground Equipment (OGE)

Launch Control Equipment (located in LCC)

Launch Enable System

Launcher and Erection Mechanism

Hydraulic Supply System

Propellant Loading System

Pressurization Control Equipment

Inertial Guidance System Checkout Equipment

Instrument Air System

Ground Power Equipment (Launch Essential)

Pad and Equipment Air Conditioning Systems

Communications Equipment (Launch Essential)

TAB "B"

b. Maintenance Ground Equipment (MGE)

MAPCHE Checkout Equipment

Re-Entry Vehicle Checkout Equipment

Propulsion System Checkout Equipment (in MAMS)

Missile Handling and Service Equipment (In MAMS)

Guidance Maintenance Equipment

Communications Equipment (non Launch Essential)

Gas and Propellant Servicing Equipment

Miscellaneous Tools and Test Equipment

Closed Circuit TV System

Pneumatic Checkout Equipment

Calibration Equipment

Work Platforms

2. Communications

- a. <u>Support Communications</u>: This system includes the Base Switching Facility, the Base Nontactical Radio Service, Off-base trucking facilities, tie lines, fire, crash, maintenance expediting and all required navigational and meteorlogical aids.
- b. Intra Complex Communications: This system consists of the conference networks, communications panels, TV Systems, direct line circuits and terminations which provide those communications functions necessary to erect, checkout and launch a missile including all circuits required for facilities and supporting operations during count down.

c. Inter-Complex Communications: These are the point-to-point systems that connect launch complexes with each other and with the support base. Systems may be government owned or commercially leased and consist of a cable or microwave radio or a combination of both.

RPIE Sub-Systems are Identified as Follows:


- a. Air Conditioning, heating and ventilation.
- b. Power generation and distribution.
- c. Water pumping and distribution.
- d. Utility air system.
- e. GOX/RP-1 and diesel vapor detection systems.
- f. Mobile Roof.
- g. Security System.
- h. Thrust section heating system.
- i. Blast detection.
- j. Flame door.
- k. Flame bucket.
- 1. Overhead handling system.
- m. Waste Disposal System.

ATLAS "E" SITE LAY-OUT

1. Facility Description and Criteria

- a. The Atlas "E!" Series Squadrons located at Warren, Forbes and Fairchild Air Force Bases consist of nine launch areas separated by approximately 14 to 18 nautical miles. Each launch area includes one horizontal-storage launcher and a launch operations building separated from the launcher by approximately 150 feet.
- b. Each launcher is earth covered except for the missile erection area which extends to the surface and is protected by special blast doors. These squadrons are equipped with the ARMA Inertial Guidance System.
- c. Each of these squadrons are supported from a squadron maintenance area located on the support base. The launcher contains propellant storage and fast loading propellant systems, and installed facility equipment to maintain the missile in a horizontal position and to erect it to a vertical position.

1 X 12 CONFIGURATION, INERTIAL GUIDANCE (TYPICAL) 550th & SUBSEQUENT SQUADRONS

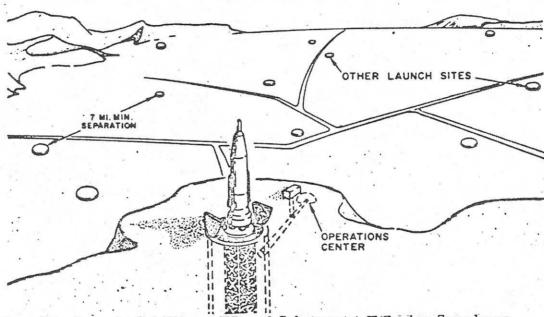

Site Layout, Schilling AFB and Subsequent F Series Squadrons

ATLAS "F" LOCATIONS

550th SCI	HILLING AFB		551st LIN	ICOLN AFB
9F	29F		19F	40F
17F	30F		22F	47F
18F	33F	7/	26F	49F
20F	37F		34F	59F
23F	46F		35F	101 F
24F	97F		38F	107 F
25F			39F	
577th AL	rus afb		578th DY	ESS AFB
/27F	62F		31F	72F
41 F	67F		53F	73F
42F	69F		54F	78F
43F	82F		55F	80F
50F	87F		64F	81 F
51F	108F		65F	94F
			71F	

92F 74F 95F				
74F 95F		28F	93F	
1 2		56F	96F	
76F 99F		70F	98F	
79F 102F		84F	100F	
85F 103F		86F	104F	
		89F	105F	
		91F		
576G VANDENBERC	AFB	576E VA	ANDENBERG AF	
106F (DAS	;)	111F	(DASO)	
STORAGE SBAMA		STORAGE GD/A		
48F 10F	in route(ABRES)	75F	114F	
68F 138F	u u	32F	112F	
12 F		60F	116F	
66F		113 F	118F	
58F		119 F		
PRODUCTION MISSI				
10 each missiles in p 122F 115F 123F		121F		

117F 120F 124F 126F

ATLAS "F" EQUIPMENT/FACILITY BREAKOUT

1. Operational Missile Area Sub-System (Ground)

Included in this broad category are two basic subdivisions: The Operational Ground Equipment which must operate successfully with the missile during readiness, count down, and launch; and the Maintenance Ground Equipment which is required to receive, service, maintain and verify the missiles and related equipment.

a. Operational Ground Equipment (OGE)

Launch Control Equipment (Located in ICC)

Missile List System

Hydraulic Supply System

Propellant Loading System

Pressurization Control System

Inertial Guidance System Checkout Equipment

Communications Equipment (Launch Essential)

Ground Power Equipment (Launch Essential)

b. Maintenance Ground Equipment (MGE)

MAPCHE Checkout Equipment

Re-entry Vehicle Checkout Equipment

Propulsion System Checkout Equipment (In MAMS)

Missile Handling and Service Equipment (In MAMS)

Guidance Maintenance Equipment

Communications Equipment (non launch essential)

Gas and Propellant Servicing Equipment

Miscellaneous Tools and Test Equipment
Pneumatic Checkout Equipment
Calibration Equipment
Work Platforms

2. Communications

- a. Support Communications: This system includes the base switching facility, the base nontactical radio service, off-base trunking facilities, tie lines, fire, crash, maintenance expediting and all required navigational and meteorological aids.
- b. Intra Complex Communications: This system consists of the conference networks, communications panels, TV Systems, direct line circuits and termination, which provide these communications functions necessary to erect, checkout and launch a missile including all circuits required for facilities and supporting operations during count down.
- c. Inter-Complex Communications: These are the point-to-point systems that connect launch complexes with each other and with the support base. Systems may be government owned or commercially leased and consist of a cable or microwave radio or a combination of both:
- 3. RPIE Sub-Systems are identified as follows:
 - a. Air Conditioning, heating and ventilation.
 - b. Power generation and distribution.
 - c. Water pumping and distribution.
 - d. Utility air system.

- e. COX/RP-1 and diesel vapor detection system.
- f. Security system.
- g. Thrust section heating system.
- h. Blast detection.
- i. Flame bucket.
- j. Overhead handling systems.
- k. Waste disposal system.
- 1. Instrument air system.
- m. Platforms.

ATLAS "F" SITE LAY-OUT

1. Facility Description and Criteria:

The 550th through 556th SMS (Series F) consists of 12 launch areas separated by approximately seven to ten N. H. Each launch area includes one vertical silo-lift type launcher and a launch operations building separated from the launcher by approximately 150 feet.

These squadrons are equipped with ARMA Inertial Guidance Systems.

Each of the squadrons are supported from a squadron maintenance area located on the support base.

NOTE: Four launch areas are in a damaged condition, three at the 579th (Walker AFB) and one at the 577th (Altus AFB).

TITAN I LOCATIONS

724th SMS Lowry AFB		125011 51125		850th S Ellsworth		
60-3654	(÷9)	60-3658	(-13)	60-3674	(-29)	
60-3655	(-10)	60-3661	(-16)	60-3677	(-32)	
60-3662	(-17)	60-3664	(-19)	60-3681	(-36)	
60-3670	(-25)	60-3666	(-21)	60-3682	(-37)	
60-3675	(-30)	60-3667	(-22)	60-3683	(-38)	
60-3691	(-46)	60-3671	(-26)	60-3684	(-39)	
61-4525	(-98)	60-3672	(-27)	60-3685	(-40)	
61-4526	(-99)	61-4528	(-101)	60-3686	(-41)	
61-4527	(-100)	60-3657	(-12)	60-3687	(-42)	
569th SM	AS	568th SMS Larson AFB		851st SMS Beale AFB		
Mt. Home						
•		- The servented		10 3/00	(-43)	
61-4496	(-69)	60-3692	(-47)	60-3688 60-3689	(-44)	
61-4497	(-70)	60-3702	(-57)	60-3693	(-44)	
61-4498	(-71)	60-3703	(-58)	60-3694	(-49)	
61-4499	(-72)	60-3704	(-59)	ALEXANDE SAME SAME	(-49) (-50)	
61-4502	(-75)	60-3706	(-61)	60-3695	(-52)	
61-4501	(-74)	60-3708	(-63)	60-3697		
61-4503	(-76)	60-3709	(-64)	60-3698	(-53)	
61-4503	(-77)	61-4492	(-65)	60-3690	(-45)	
61-4506	(-79)	61-4494	(-67)	60-3699	(-54)	
395 A		Lowry AFE				
Bandenberg AF	В	Ellsworth A				
	-	Mt. Home				
60-3660	(1-15)	Larson AF		P		
60-3665	(-20)	Beale AFB	10			
60-3668	(-23)	Vandenberg				
		SBAMA Sto	rage 28	-		

Total

86

TITAN I EQUIPMENT/FACILITY BREAKOUT

l. Aerospace Ground Equipment:
The aerospace Ground Equipment (AGE) is all that equipment required on the ground to make the weapon system operational in its actual environment. This includes all equipment required to install, launch, arrest, control, inspect, test, adjust, calibrate, measure, assemble, disassemble, handle, transport, safeguard, store, maintain or operate the various elements of the weapon system.

Included in this broad category are two basic subdivisions: The Operational Ground Equipment which must operate successfully with the missile during readiness, countdown and launch, and the Maintenance Ground Equipment which is required to receive, service, maintain and verify the missiles and related equipment.

a. Operational Ground Equipment (OGE):

For Titan I, the following major elements comprise the OGE:

Launch Control Equipment (located in LCC)

Launch Enable System

Launch System

Hydraulic Supply System

Propellant Loading System

Pressurization Control Equipment

Ground Guidance System

Pad and Equipment Air Conditioning Systems.

Communications Equipment (Launch Essential)

Ground Power Equipment (Launch Essential)

b. Maintenance Ground Equipment (MGE):

Launch Control Checkout Equipment

Re-entry Vehicle Checkout Equipment

Propulsion System Checkout Equipment

Missile Handline and Service Equipment

Guidance Maintenance Equipment

Communications Equipment (non-launch essential)

Propellant Servicing Equipment

Miscellaneous Toos and Test Equipment

Pneumatic Checkout Equipment

Calibration Equipment

Work Platforms

2. Communications:

The Titan I Communication System is composed of a hardened cable system between launch complexes with a comon support base, and between the support base and each launch complex; Launch Enable System (LES); Primary Alert System (PAS); SAC Telephone Net (STN); SAC Control System (SACCS); high frequency single sideband radio and ultra high frequency radio; TV Systems; public address system; direct line telephone system; dial line telephone system; maintenance networks, and common carrier (telephone company) long lines to connect the support base and associated launch sites to Hq SAC and numbered Air Forces.

- a. The Launch Enable System (LES) is basically a group of tine transmitters and receivers connected in such a way that tones generated at the Command Post (CP) and the Alternate Command Post (ACP) are received at each launch site, energize a relay which inhibits the launch sequence and acknowledges receipt of the tone back to the CP and ACP.
- b. The Primary Alert System (PAS) consists of speakers, telephone handsets and recorders. Signals are received from SAC and numbered Air Forces at

the CP, the ACP, and all associated launch complexes simultaneously and are recorded.

- c. The SAC telephone net (STN) enters the CP via common carrier long lines and terminates on a switchboard from which it is extended to individual subscribers.
- d. The public address system is composed of amplifiers and speakers located throughout each launch complex and accessed from the launch console, the guidance console or the equipment and facilities console.

3. Real Property Installed Equipment (RPIE):

- a. RPIE subsystems are identified as follows:
 - (1) System I Electrical Power Generation and Distribution
 - (2) System II Heating, Ventilating and Air Conditioning
 - (3) System III- Water Supply, Distribution and Waste
 - (4) System IV Sensing, Warning and Blast Protection
 - (5) System V Mechanical

SITE LAY-OUT

- 1. Missile Silo
- 2. Utilities Tunnel
- 3. Equipment Terminal
- 4. Missile Silo Branch Tunnel
- 5. Equipment Terminal Branch Tunnel
- 6. Tunnel Junction l
- 7. Missile Launcher | Branch Tunnel
- 8. Tunnel Junction 2
- 9. Propellant Terminal Branch Tunnel
- 10. Propellant Terminal
- 11. Lox Storage Area
- 12. Lox Fill and Vent Shaft
- 13. Lox Tunnel
- 14. Blast Lock 2
- 15. Missile Launcher 2 Branch Tunnel
- 16. TunneldJunction 5
- 17. Tunnel Junction 4

- 18. Service Road
- 19. Tunnel Junction 7
- 20. Missile Launcher 3 Branch Tunnel
- 21. Tunnel Junction 9
- 22. Sewage Stabilization Pond
- 23. Tunnel Junction 8
- 24. Missile Launcher 3 Tranch Tunnel
- 25. Main Tunnel
- 26. Tunnel Junction 13
- 27. Tunnel Junction 12
- 28. Power House Air Filtration facility.
- 29. Water Storage Tanks
- 30. Portal
- 31. No. 2 Diesel Oil Tank
- 32. Blast Lock 3
- 33. No. 4 Diesel Oil Tank

TAB "D"

- 34. Tunnel Junction ll
- 35. Power House Exhaust
- 36. Antenna Silo 2
- 38. Antenna Silo l
- 39. Tunnel Junction 10

- 40. Nitrogen Blacket Tank
- 41. Missile Fuel Storage Tank
- 42. Launcher Area Air Filtration Facility
- 43. Blast Lock 1


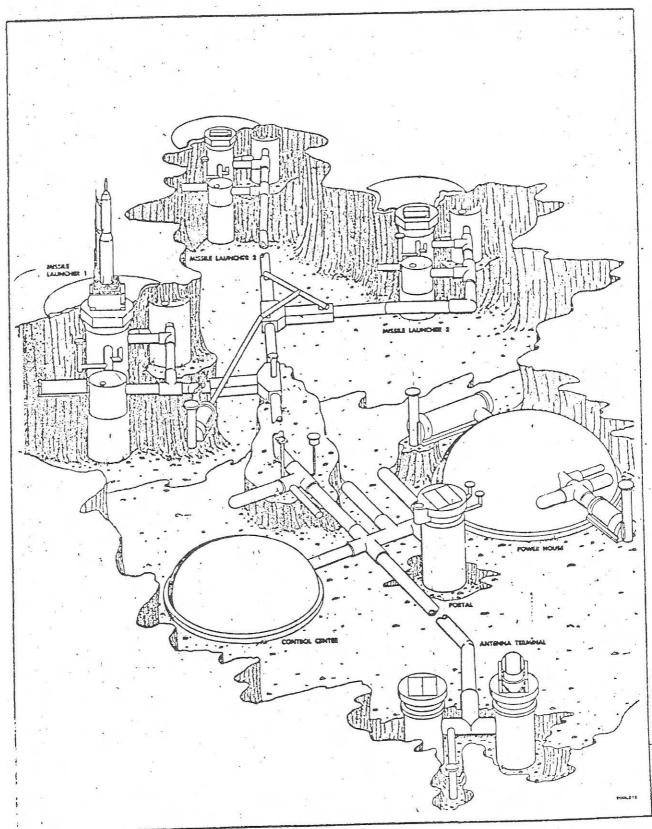


Figure 1-4. Operational Base Launch Complex (Sheet 3 of 3)



Operational Base Launch Complex (Sheet 1 of 3)

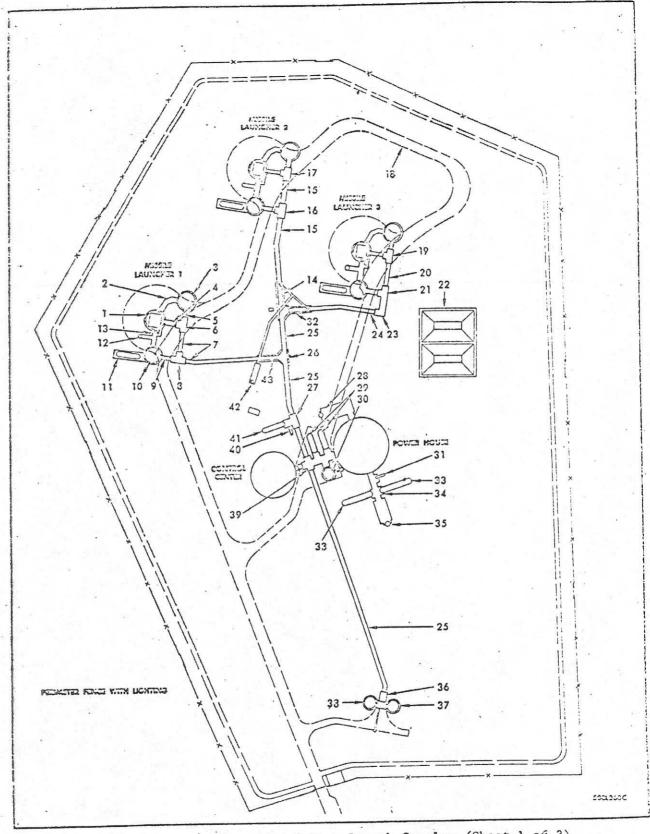
